




Exercise

It's time to bring iterations into play on Tom's Trails. Each of the features that Tom wants for Trails Online has had estimates added to specify how long it will take to actually develop. Then we figured out how important each is to Tom and then assigned a priority to each of them (10 being the highest priority, 50 being the lowest). Take each feature and position them along the project's timeline, adding an iteration when you think it might be useful.

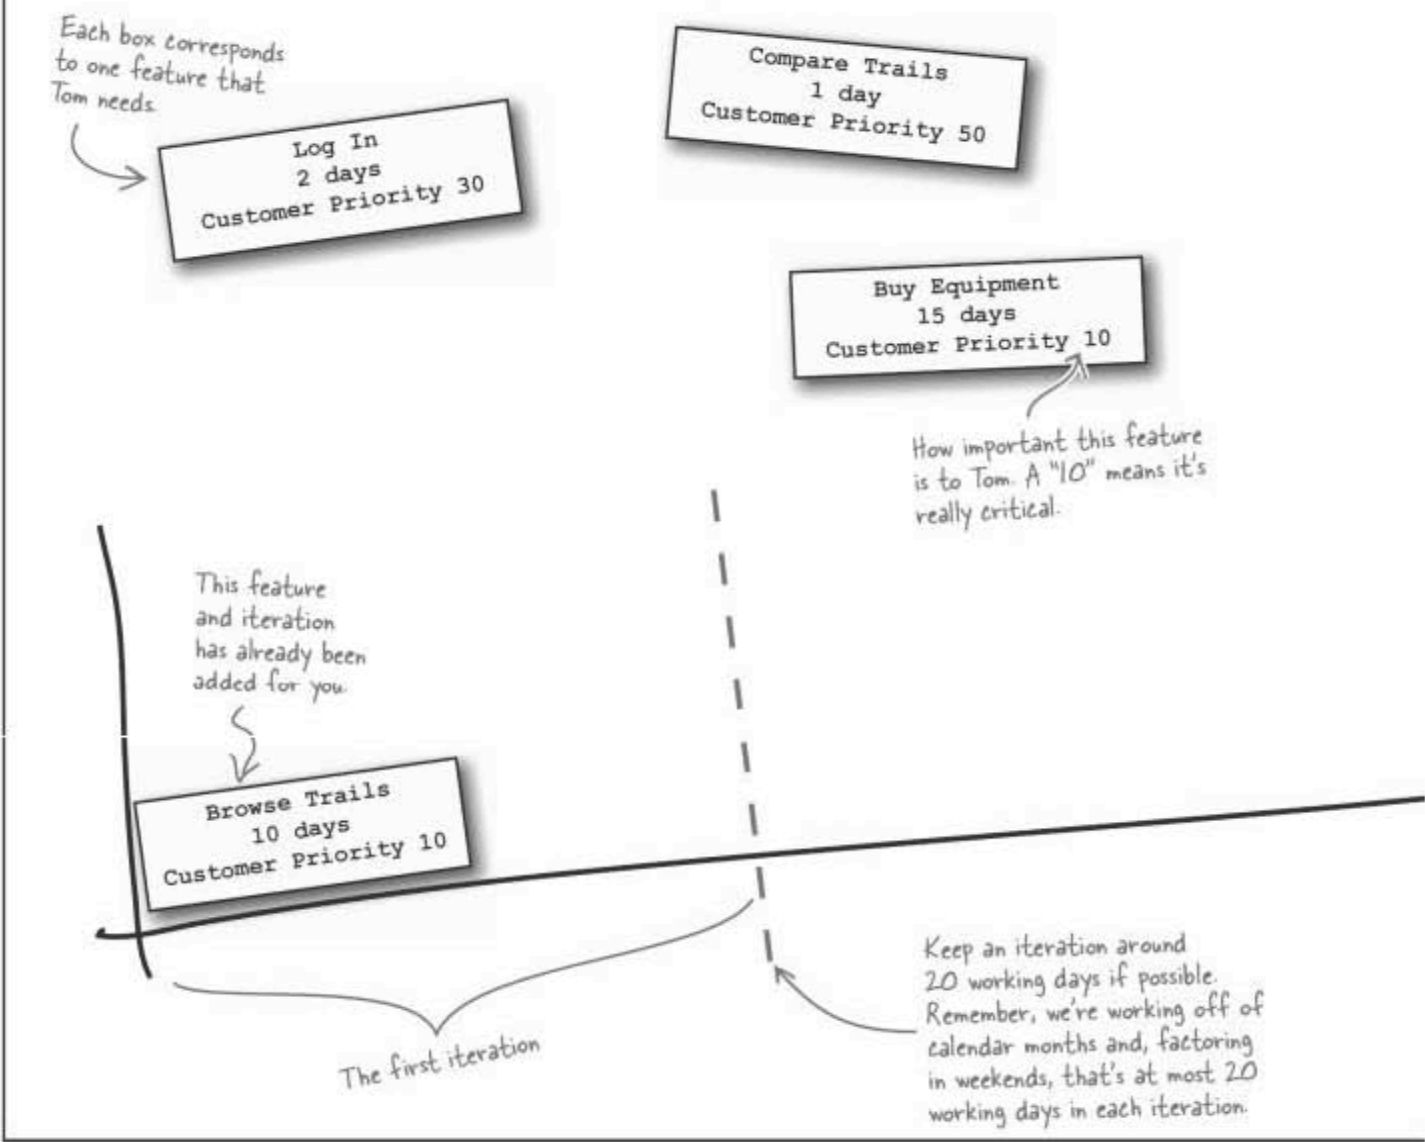

Oh, one other thing. Tom doesn't want customers to be able to buy equipment unless they've logged in to the web site. Be sure and take that into account in your plan.

Each feature has an estimate to show how long it should take to develop that feature (in actual working days).

List Equipment
7 days
Customer Priority 10

Add a Review
2 days
Customer Priority 20

View Reviews
3 days
Customer Priority 20

Search Trails
3 days
Customer Priority 20

10 is high priority, 50 is low. We'll look at why these priorities are in increments of 10 in Chapter 3.

Don't forget to add as many iterations as you think will be useful.
